

Monthly Report

April 2023


What's Happening

- Continued elevated deck pours
- Continued foundations at Garage
- Poured multiple foundation walls at garage
- Backfill South side of project - Multiple deliveries along Farnsleigh



Key Features/Milestones

- Completed all slab on grade pours
- Completed deck pours lvl 1 East and West
- Started Garage foundation walls

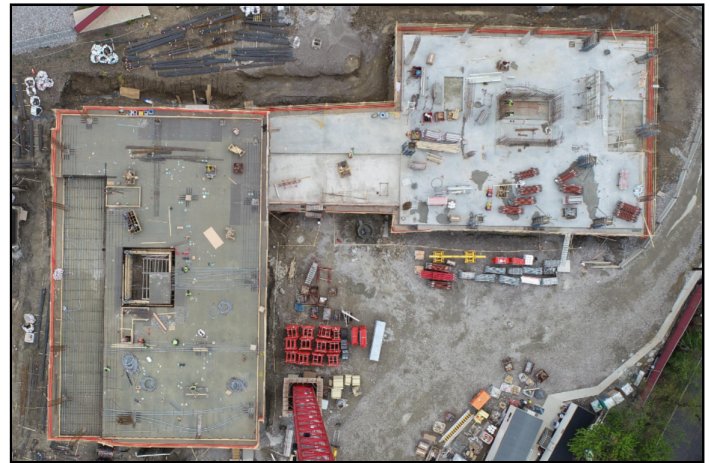

Van Aken District Phase Two Three-Month Construction Look Ahead

2023												
May				June				July				
01	08	15	22	29	5	12	19	26	03	10	17	24
Concrete Structure 3-4				Concrete Structure 5-6				Concrete Structure 7-8				
<ul style="list-style-type: none"> • Start slab on grade at Parking Garage • Complete concrete pours at level 3, both West and East towers • Complete concrete pours at level 4, both West and East towers • Complete backfill South side of project, complete generator wall 				<ul style="list-style-type: none"> • Continue concrete pours at Parking Garage • Complete concrete pours at level 5, both West and East towers • Complete concrete pours at level 6, both West and East towers 				<ul style="list-style-type: none"> • Finish Parking Garage • Complete concrete pours at level 7, both West and East towers • Complete concrete pours at level 8, both West and East towers 				

For questions and comments, please email us at com-inbound-van-aken-district@procoretech.com
 Visit <https://www.vanakenphasetwo.com/construction-updates> for construction updates
