

Monthly Report


December 2022

What's Happening

- Concrete contractor has started work
- Concrete pours at elevator pits
- Concrete foundations & lower Walls
- Excavation of garage East of building site

Key Features/Milestones

- Completion of 95 deep foundations
- Excavation of both elevator pits
- Completion of mass excavation at towers
- Installation of tower crane

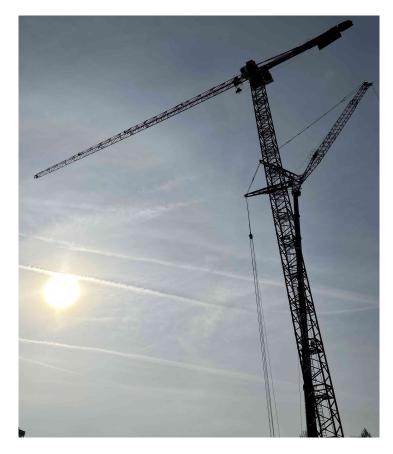

Van Aken District Phase Two Three-Month Construction Look Ahead 2023 January February March Start elevator pits for both Continue underground plumbing Continue Slab on Grade and electrical work concrete pours towers Start concrete foundations and · Continue concrete pours, lower Continue concrete structure, lower wall pours walls start to go vertical (2nd floor) Start underground sanitary and • Start pouring Slab on Grade storm. Connection to street concrete Mass excavation – continue at · Complete underground sanitary connection at street Garage
