


January 2023

Monthly Report

What's Happening

- Continue concrete foundations
- Continue concrete walls & columns
- Starting underground

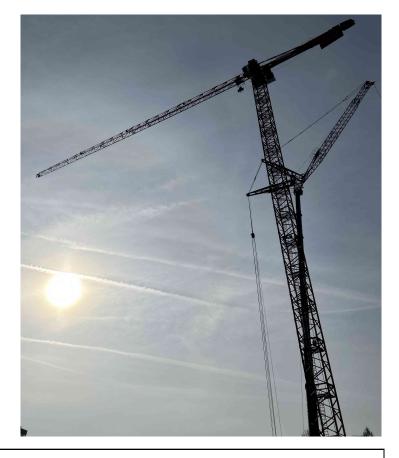

Key Features/Milestones

- Completed pouring elevator cores
- Completed lagging at the parking garage

Van Aken District Phase Two

Three-Month Construction Look Ahead

2023													
February				March				April					
03	10	17	24	03	10	17	24	31	07	14	21	28	
Foundations – Concrete Structure Concrete Structure & SOG Vertical Structure & Parking Garage													
 Complete elevator pits for both towers Complete foundations and lower wall pours Begin columns and shear walls Start underground sanitary and storm. 				 Complete underground plumbing and electrical work Start pouring Slab on Grade concrete Start fabrication of façade system Begin foundation at garage 					 Continue concrete structures, move vertical Continue parking garage concrete pours 				

For questions and comments, please email us at <u>com-inbound-van-aken-district@procoretech.com</u> Visit <u>https://www.vanakenphasetwo.com/construction-updates</u> for construction updates
